



Customer



Location



W.O. #


Work Order Overview:

Removed old water treatment equipment. Replaced with new Smart Release Water Treatment Station. Removed non working water meter. Replaced with new meter. Added CL001P closed loop inhibitor to the chilled water system. Changed both filters. Removed drift eliminators from cooling tower. Took off site. Soaked them in a sulfamic / glycolic acid bath. Pressure washed drift eliminators. Resoaked drift eliminators and pressure washed again. Some had to be soaked for a 3rd time. Drift eliminators were re installed. Circulated descaler through system to improve water/air flow through fouled tower fill.


New Treatment Station



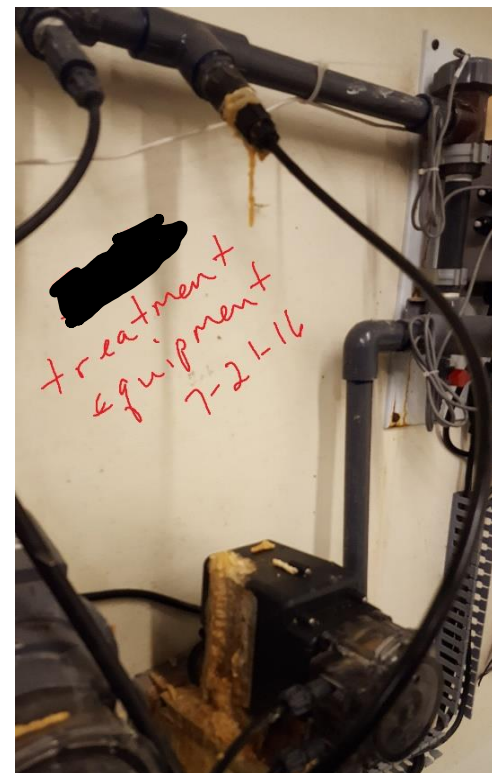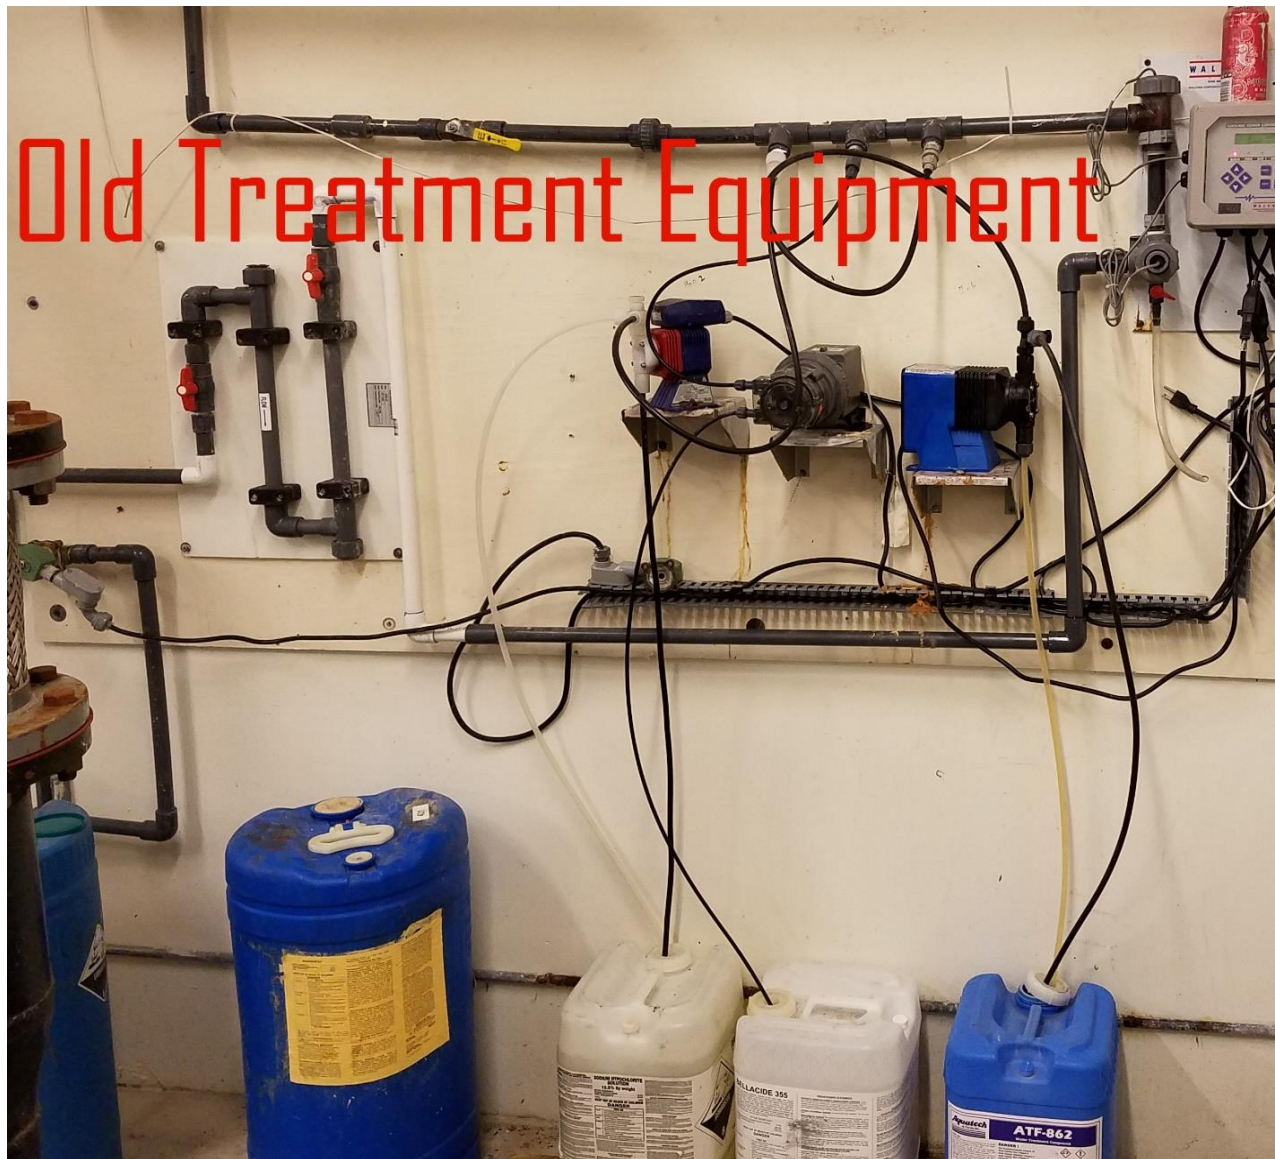


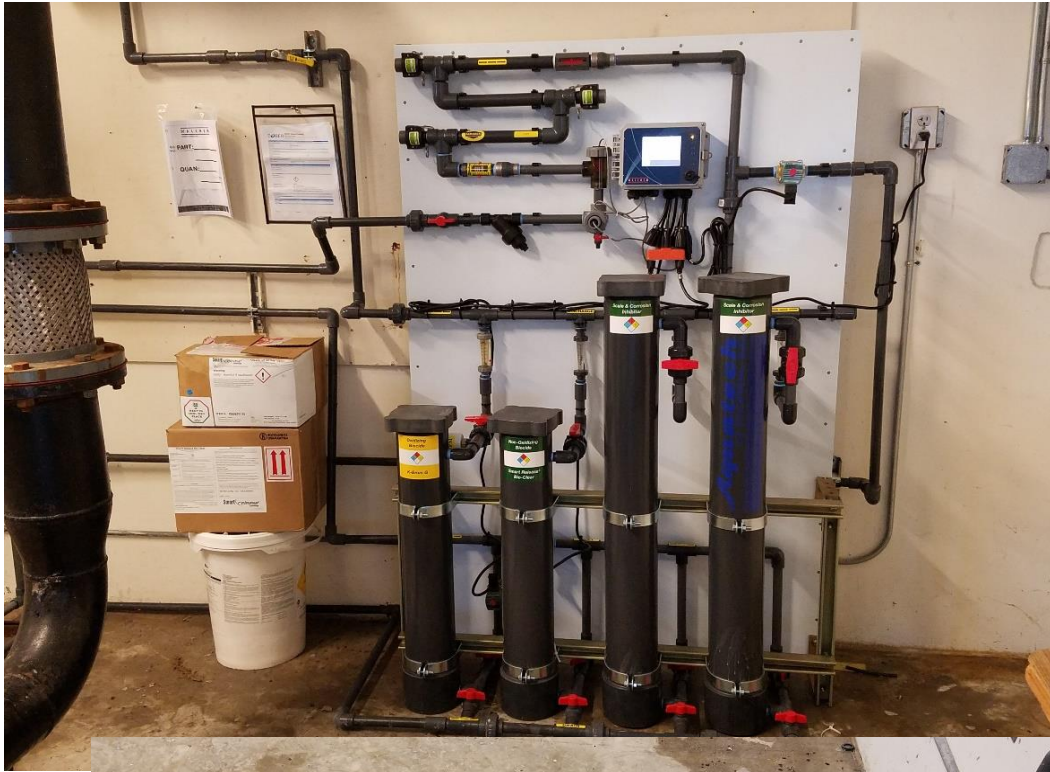

Drift Eliminators before cleaning

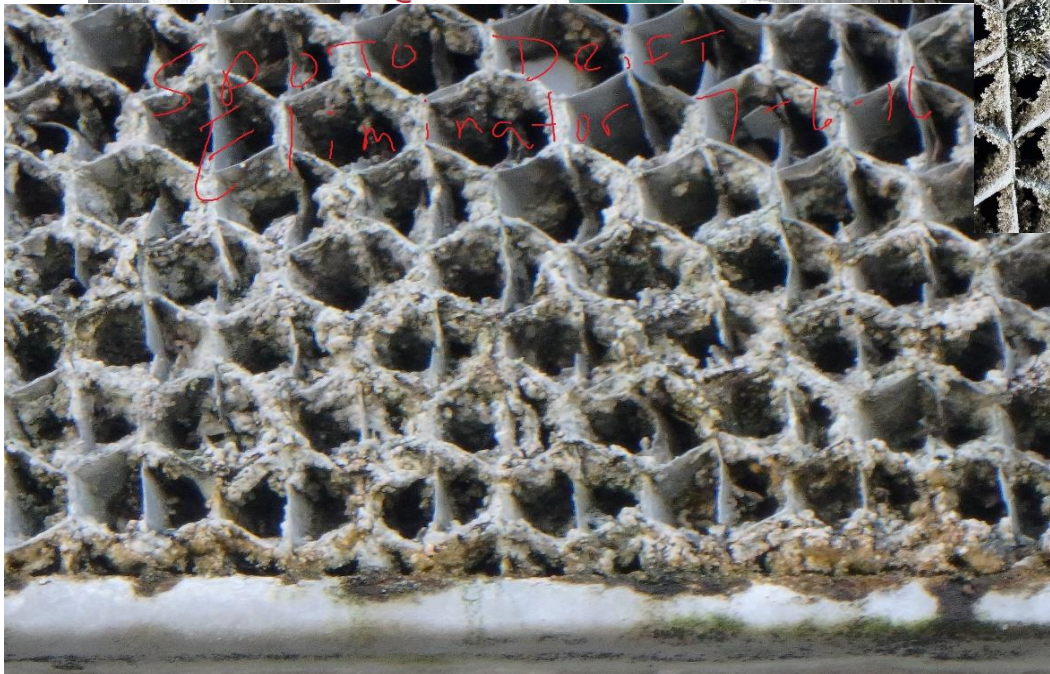

Drift Eliminator Cleaning

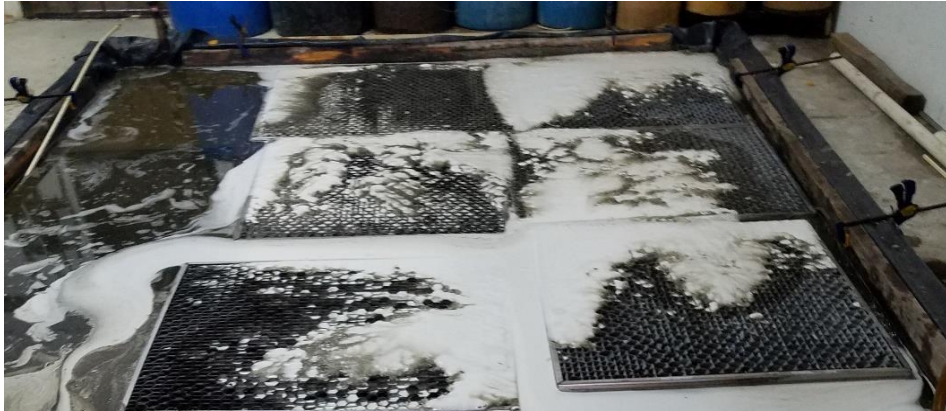


Re Soak



2nd Set





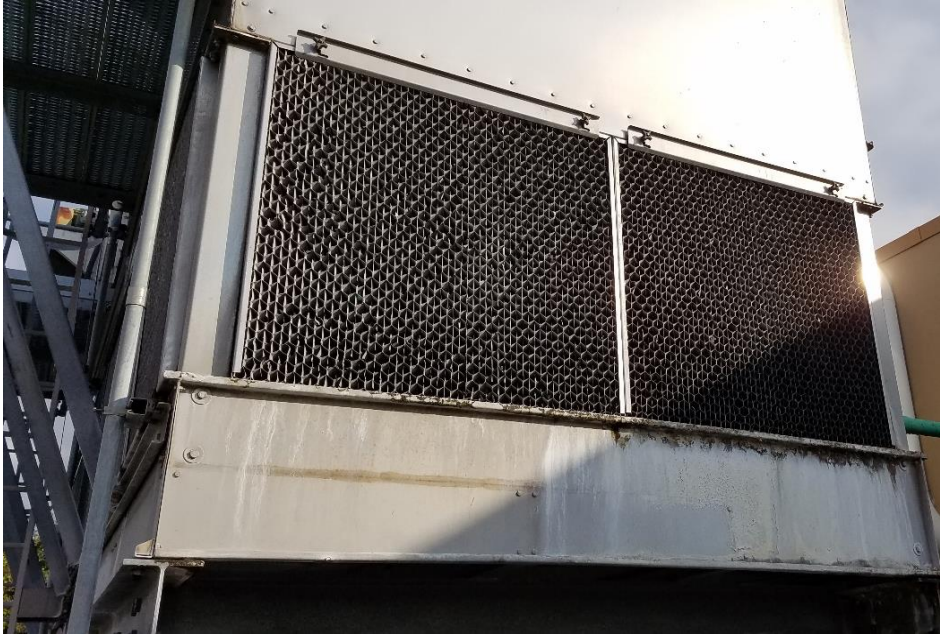

Tower Fill Descaling

